

College of Marin
Measure C
Bond Modernization Program
Progress Update


April 12, 2011
Indian Valley Campus Community
Forum

IVC Campus: Construction Complete

- New Main Building completed in January, 2011.
- Minor construction items and site work – ongoing.
- Assess & maintain existing buildings.

IVC Campus Map

New buildings circled in orange.

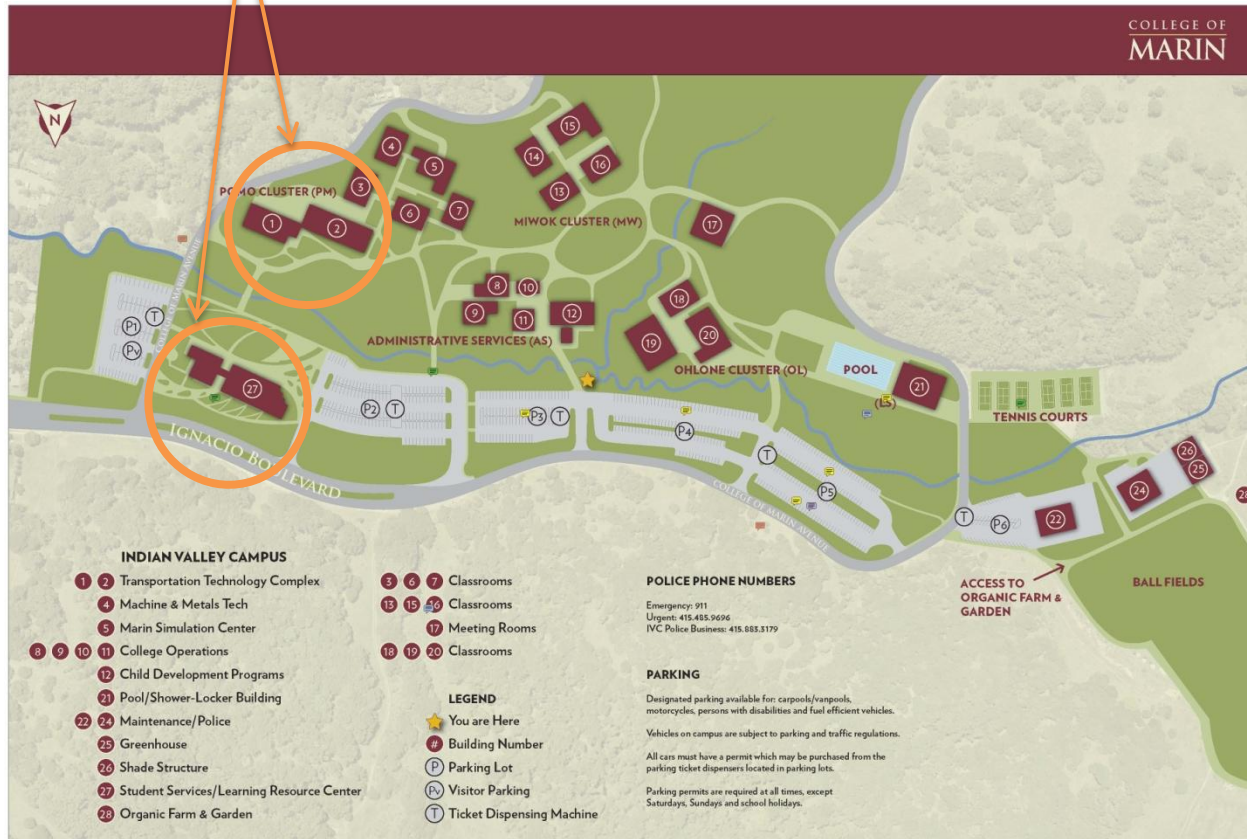

IVC Campus Map *after program completion*



Kentfield Campus

- Recent Board Actions
- Projects in Construction
- Projects in Design


Recent BOT Actions

1. Approved Child Study Center – Larkspur Annex site.
2. Approved New Academic Center for design & Construction (43,170 gross square feet).
3. Approved \$1.25M budget for re-surfacing of track.
4. Approved \$1M budget for ADA improvements.
5. Approved removal of modular buildings.
6. Approved structural-improvement funding for the Austin Science Center and “paint and patch” funding to “freshen up” the building while being used as swing space.

Projects in Construction

- Science/Math/Central Plant Complex

- Current activity: Structural framing and decking.
- Construction: Spring 2010 to Fall 2012
- Move in: Fall and Winter 2012

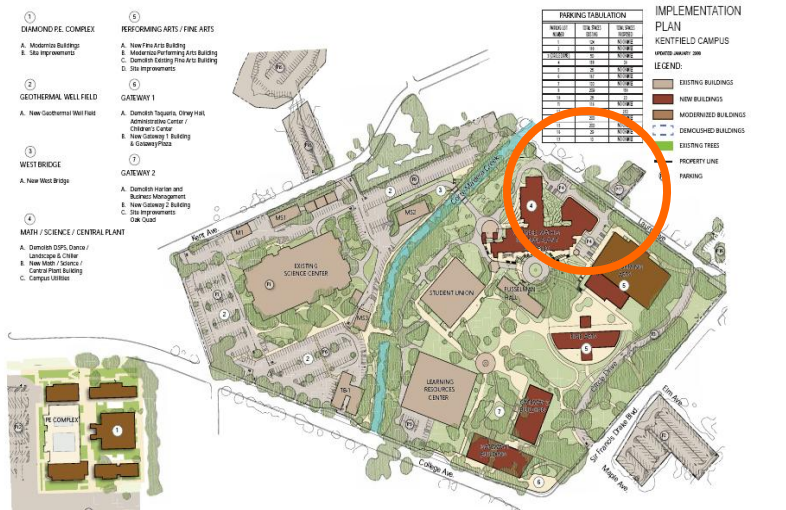

Projects in Design

- **Child Study Center (CSC)**
 - 6,180 gsf, plus outdoor playspace
 - Location: Larkspur Annex site
 - Design phase: Spring 2011 – Fall 2011
 - Construction: Winter 2012 – Fall 2012
- **New Academic Center (NAC)**
 - 43,170 gsf, 16 general purpose classrooms
 - Location: NE corner of campus
 - Design phase: Spring 2011 – Fall 2012
 - Construction: Winter 2012 – Summer 2014
