

College of Marin
Measure C
Bond Modernization Program
Progress Update

October 27, 2011

Kentfield Campus Community Forum

Agenda

- Under Construction
- Projects in Design + Timelines
- Q & A

Under construction

- Kentfield:
 - Performing Arts
 - Science Math Central Plant
 - Track



PA Demoliton




PA Modernization

Under Construction - Kentfield

- Science/Math/Central Plant Complex

- Current activity: Structural Steel Complete
- Construction: Spring 2010 to Fall 2012
- Move in: Winter 2012

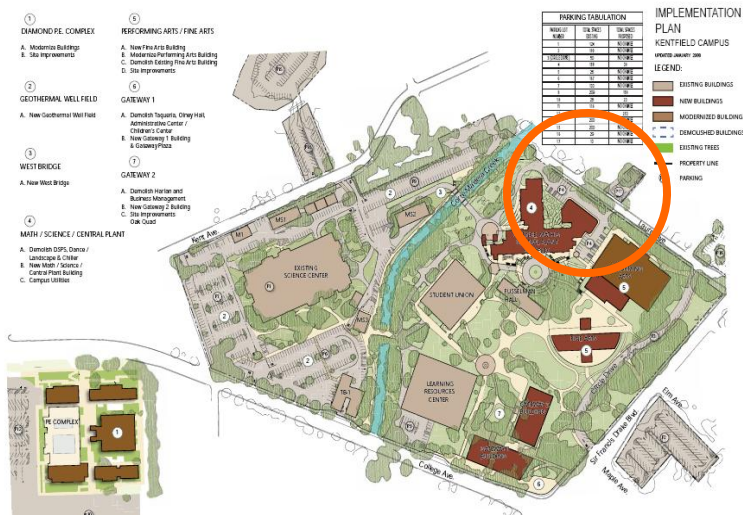

Kentfield – Track & bleacher demo project



Projects in Design + Timelines

- Kentfield
 - Child Study Center
 - New Academic Center

Design Phase-

Kentfield, Larkspur Annex site

- **Child Study Center**
 - Design: Fall 2010-Fall 2011
 - Construction: Fall 2012-spring 2013
 - Move in: Spring 2013



Design Phase-

Kentfield, New Academic Center

- Design: Fall 2010-
- Construction: Fall 2012-spring 2013
- Move in: Spring 2013
